



SH 130 Segment 4 Opening Scheduled for April


On April 30, TxDOT plans to open the final segment of the CTTS SH 130 project. This 8.7-mile segment extends SH 130 from SH 71 south to US 183 near Mustang Ridge. During May and June, drivers on this portion of SH 130 will be able to travel toll-free. TxTag account holders will continue to be able to use Segment 4 toll-free through July and will pay a 50 percent discounted toll in August. Drivers without a TxTag will be charged full tolls beginning on July 1.

In this segment, all of the bridge riding surfaces have been completed with the exception of the eastbound and westbound SH 45SE mainlane bridges over US 183. Work is expected to begin on placement of the remaining 10 spans on these bridges in mid-April when traffic on US 183 is switched to the new northbound frontage road.

During March, asphalt was placed at Maha Loop, Moore Road, and the US 183 northbound frontage road. Concrete



Paving Operations, Northbound Mainlanes between Maha Loop and US 183

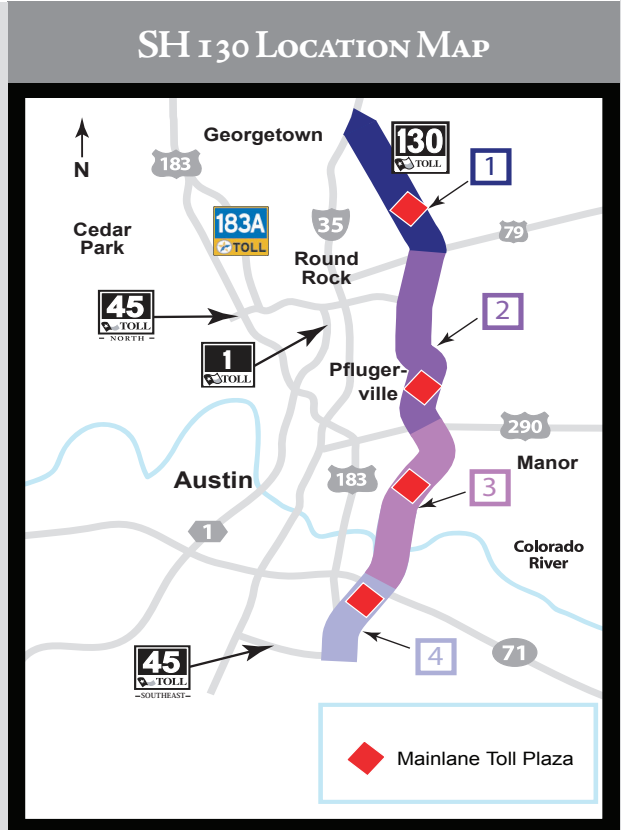

paving continued on the mainlanes between Von Quintus Road and US 183. The new Elroy Road bridge over SH 130 was completed and opened to traffic in March.

April activities are focused on final preparations for the opening of Segment 4. Crews are completing slope work, installing lighting, erecting signs, and finishing grooving and sealing of bridge riding surfaces. Asphalt work is being completed at Pearce Road, on the mainlane toll plaza ramps, and on the the ramps connecting SH 130 to US 183.

(cont'd on page 2)



*This report is for the Central Texas Turnpike System, 2002 Project (CTTS-2002 Project). For more complete information on the CTTS-2002 Project, refer to the Official Statement or the latest quarterly report (www.centraltexasturnpike.org). Information is also available from the State Information Depository and the Nationally Recognized Municipal Securities Information Repositories. No financial decision should be made based upon this report. For further information, contact the TxDOT Austin District Public Information Office: 512.832.7060.

Note: Segments 5 and 6 of SH 130, SH 45N Section 8 direct connectors, SH 45N Section 9, SH 45SE, and 183A are not part of the CTTS 2002 Project and are not funded through the Series 2002 Obligations. Information on these roadways may be included in this report because these facilities are major connector projects and are important to the overall CTTS.

SH 130 Update

With the opening of SH 130 Segment 4, all of the Central Texas Turnpike System 2002 Project will be open to traffic. Work will continue through the next few months on completing the SH 130/US 183/SH 45SE interchange. Construction of SH 45SE from SH 130/US 183 west to I-35 is underway and scheduled for completion in the Spring of 2009. Right of way acquisition for extension of SH 130 through Caldwell and Guadalupe counties to I-10 near Seguin is in progress, and construction on this portion of SH 130 is expected to begin in 2009. Visit www.mysh130.com for additional information on the Caldwell/Guadalupe county segments of SH 130.



*Bridge Deck Slab Grooving Operation
Elroy Road Bridge over SH 130*

OTHER SH 130 ACTIVITIES

During March, the Developer also completed the striping for new lanes at the SH 130/US 290 interchange; all lanes are now open (Segment 2). In Segment 3, bridge crews completed erecting the steel girders on the SH 71/SH 130 direct connector and began preparations for placing the final remaining riding surfaces.



Deck Slab Placement SH 130/SH 71 Direct Connector

SH 45N/Loop 1 Update

Sections 1, 2, 3, 5, 7 and 8 are complete and have either been accepted by TxDOT or are in the process of final acceptance.

In Section 4, work continues on the roadway improvements at I-35 and Hesters Crossing Boulevard. Excavation for the southbound collector-distributor roadway has begun. Bent cap and column construction for the westbound lanes of the new Hesters Crossing bridge continued in March, as did work on the new alignment for the I-35 southbound frontage road.



*Bent Cap Construction,
Hesters Crossing Bridge*



*Excavation work for
Collector-Distributor
Roadway at
Hesters Crossing*

Construction of the new westbound entrance and eastbound exit ramps at SH 45N and Heatherwilde Boulevard is nearing completion. In March work activities included topsoil placement and seeding operations, placement of riprap and railing, and construction of signal foundations. Work also proceeded on final preparations for completion of the ramp toll facilities.

TURNPIKE TEAM
2002 PROJECT BOND OVERSIGHT
General Engineering Consultant: PBS&J

SH 130
Program Manager: HDR Engineering, Inc.
Developer: Lone Star Infrastructure

SH 45N & LOOP 1
Construction Manager: PBS&J

TxDOT AUSTIN DISTRICT
CTTS PROJECT OFFICE
1421 Wells Branch Parkway Bldg., 1, Ste. 107
Pflugerville, Texas 78660
512.225.1300
www.centraltexasturnpike.org

central texas
turnpike system
